



**UU-AMP8-ROSS-DEL-1002-001978-1**

**Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31**



**UU-AMP8-ROSS-DEL-1002-001978-1**

## Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

| Activity ID | Activity Name                                                                                       | Remaining Duration                                                                                              | Start | Finish       | Total Float | 2025   |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        | 2026   |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|-------------|-----------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------|-------|--------------|-------------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|---|---|--------|--------|--------|--------|--------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
|             |                                                                                                     |                                                                                                                 |       |              |             | Nov 17 | Nov 24 | Dec 01 | Dec 08 | Dec 15 | Dec 22 | Dec 29 | Jan 05 | Jan 12 | Jan 19 | Jan 26 | Feb 02 | Feb 09 | Feb 16 | Feb 23 | Mar 02 | Mar 09 | Mar 16 | Mar 23 | Mar 30 | Apr 06 | Apr 13 | Apr 20 | Apr 27 | May 04 | M | M | May 25 | Jun 01 | Jun 08 | Jun 15 | Jun 22 |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1870                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 5d    | 12-Jan-2026  | 16-Jan-2026 | 5d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1880                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 19-Jan-2026 | 11d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1230                                                                              | Section 168 - Power to Access to Carry Out Surveys Shaft2 ((Broadwater Woods)                                   | 7d    | 20-Jan-2026  | 26-Jan-2026 | 15d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | THE LANCASHIRE COUNTY COUNCIL -Access to Shaft 2, BH103, BH104 and BH105 is via. Title No. LAN96754 |                                                                                                                 | 11d   | 12-Jan-2026  | 26-Jan-2026 | 11d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1890                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 5d    | 12-Jan-2026  | 16-Jan-2026 | 5d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1900                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 19-Jan-2026 | 11d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1910                                                                              | Section 168 -Power to Access to Carry Out Surveys Shaft2 ((Broadwater Woods)                                    | 7d    | 20-Jan-2026  | 26-Jan-2026 | 15d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | UNKOWN LANDOWNER - Access is also via an unnamed parcel of land                                     |                                                                                                                 | 11d   | 12-Jan-2026  | 26-Jan-2026 | 11d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1920                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 5d    | 12-Jan-2026  | 16-Jan-2026 | 5d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1930                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 19-Jan-2026 | 11d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1940                                                                              | Section 168 -Power to Access to Carry Out Surveys Shaft2 ((Broadwater Woods)                                    | 7d    | 20-Jan-2026  | 26-Jan-2026 | 15d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | WYRE BOROUGH COUNCIL - BH 106 and CPT 101 are within Title No. LAN31019                             |                                                                                                                 | 11d   | 12-Jan-2026  | 26-Jan-2026 | 5d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1960                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 5d    | 12-Jan-2026  | 16-Jan-2026 | 5d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1970                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 19-Jan-2026 | 5d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1950                                                                              | Section 168 -Power to Access to Carry Out Surveys Shaft2 ((Broadwater Woods)                                    | 7d    | 20-Jan-2026  | 26-Jan-2026 | 7d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | Shaft 3 & Shaft 4                                                                                   |                                                                                                                 | 16d   | 05-Jan-2026  | 26-Jan-2026 | 38d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | THE LANCASHIRE CC - BH107, BH108, BH109, BH110 and CPT102 are within Title No. LAN81504             |                                                                                                                 | 11d   | 12-Jan-2026  | 26-Jan-2026 | 33d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1980                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 5d    | 12-Jan-2026  | 16-Jan-2026 | 33d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-1990                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 19-Jan-2026 | 33d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2000                                                                              | Section 168 -Power to Access to Carry Out Surveys Shaft3 & 4 Cardinal Allen Catholic High School Playing Fields | 7d    | 20-Jan-2026  | 26-Jan-2026 | 45d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | LANCASTER ROMAN CATHOLIC DIOCESAN TRUSTEES - land off Melbourne Avenue                              |                                                                                                                 | 11d   | 12-Jan-2026  | 26-Jan-2026 | 33d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2010                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 5d    | 12-Jan-2026  | 16-Jan-2026 | 33d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2020                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 19-Jan-2026 | 33d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2030                                                                              | Section 168 -Power to Access to Carry Out Surveys Shaft3 & 4 Cardinal Allen Catholic High School Playing Fields | 7d    | 20-Jan-2026  | 26-Jan-2026 | 45d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | BLACKPOOL BOROUGH COUNCIL -Tramway LAN78634                                                         |                                                                                                                 | 22d   | 05-Jan-2026  | 26-Jan-2026 | 52d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2070                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 11d   | 05-Jan-2026* | 15-Jan-2026 | 0d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2080                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 16-Jan-2026 | 52d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2090                                                                              | Section 168 -Power to Access to Carry Out Surveys - Tramway                                                     | 8d    | 19-Jan-2026  | 26-Jan-2026 | 52d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | ELECTRICITY NORTH WEST LIMITED - Electricity Sub station land at South Strand LAN56055              |                                                                                                                 | 21d   | 05-Jan-2026  | 25-Jan-2026 | 53d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2100                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 11d   | 05-Jan-2026  | 15-Jan-2026 | 53d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2110                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 16-Jan-2026 | 53d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2120                                                                              | Section 168 -Power to Access to Carry Out Surveys - ENW                                                         | 7d    | 19-Jan-2026  | 25-Jan-2026 | 53d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | Shaft 5,6 & 7                                                                                       |                                                                                                                 | 22d   | 05-Jan-2026  | 26-Jan-2026 | 0d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | THE CORPORATION OF ROSSALL SCHOOL - BH111 - BH118, CPT103,CPT104, CBR10 &102 in Title No. LAN8657   |                                                                                                                 | 22d   | 05-Jan-2026  | 26-Jan-2026 | 0d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2040                                                                              | Produce 168 Drawings and Issue to UU                                                                            | 11d   | 05-Jan-2026  | 15-Jan-2026 | 0d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2050                                                                              | UU Serve Notice to Landowner                                                                                    | 0d    |              | 19-Jan-2026 | 0d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | AMP8-DD&B-ROS-ECI-2060                                                                              | Section 168 -Power to Access to Carry Out Surveys Shaft5,6 & 7 - Rossall School                                 | 7d    | 20-Jan-2026  | 26-Jan-2026 | 0d     |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | Section 159                                                                                         |                                                                                                                 | 16d   | 13-Jan-2026  | 03-Feb-2026 | 104d   |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|             | Shaft 1                                                                                             |                                                                                                                 | 16d   | 13-Jan-2026  | 03-Feb-2026 | 70d    |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |   |   |        |        |        |        |        |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

Remaining Level of Effort

 Construction summary, Team #1

Construction summary, Team #2

 Construction summary, Team #3

Actual Level of Effort

Actual ...

 Remai...

Critical...

Milesto...

Programme ref: Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

Project ID: UU-AMP8-ROSS-DEL-1002-001978-1

Data Date: 24-Nov-2025

Page 2 of 11

Date

23-Feb-2026

Revision

Rossall CL31

Checked

SI

Approved



## Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

| <div> <div> <div>Remaining Level of Effort</div> <div>Construction summary, Team #1</div> <div>Construction summary, Team #2</div> <div>Construction summary, Team #3</div> <div>Actual Level of Effort</div> </div> <div> <div>Actual ...</div> <div>Remai...</div> <div>Critical...</div> <div>Milesto...</div> </div> </div> | <div> <div>Programme ref: Rossall Outfall Pipe Installation &amp; Relining- 24th Nov 25 - CL 31</div> <div>Project ID: UU-AMP8-ROSS-DEL-1002-001978-1</div> </div> | <div> <div>Data Date: 24-Nov-2025</div> <div>Page 3 of 11</div> </div> | <table border="1"> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> <tr> <td>23-Feb-2026</td> <td>Rossall CL31</td> <td>SI</td> <td></td> </tr> <tr> <td colspan="4"></td> </tr> </table> | Date | Revision | Checked | Approved | 23-Feb-2026 | Rossall CL31 | SI |  |  |  |  |  |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------|----------|---------|----------|-------------|--------------|----|--|--|--|--|--|
| Date                                                                                                                                                                                                                                                                                                                            | Revision                                                                                                                                                           | Checked                                                                | Approved                                                                                                                                                                                                               |      |          |         |          |             |              |    |  |  |  |  |  |
| 23-Feb-2026                                                                                                                                                                                                                                                                                                                     | Rossall CL31                                                                                                                                                       | SI                                                                     |                                                                                                                                                                                                                        |      |          |         |          |             |              |    |  |  |  |  |  |
|                                                                                                                                                                                                                                                                                                                                 |                                                                                                                                                                    |                                                                        |                                                                                                                                                                                                                        |      |          |         |          |             |              |    |  |  |  |  |  |



**UU-AMP8-ROSS-DEL-1002-001978-1**

## Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

| Activity ID                                                                                       | Activity Name                                                         | Remaining Duration | Start        | Finish      | Total Float |
|---------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------|--------------------|--------------|-------------|-------------|
| AMP8-DD&B-ROS-ECI-2540                                                                            | Access Protection Survey Required                                     | 5d                 | 28-Jan-2026  | 03-Feb-2026 | 104d        |
| Shaft 5 &7                                                                                        |                                                                       | 12d                | 14-Jan-2026  | 29-Jan-2026 | 82d         |
| THE CORPORATION OF ROSSALL SCHOOL - BH111 - BH118, CPT103,CPT104, CBR 10 &102 in Title No.LAN8657 |                                                                       | 12d                | 14-Jan-2026  | 29-Jan-2026 | 82d         |
| AMP8-DD&B-ROS-ECI-2420                                                                            | Produce 159 Drawings and Issue to UU                                  | 5d                 | 14-Jan-2026  | 20-Jan-2026 | 4d          |
| AMP8-DD&B-ROS-ECI-2430                                                                            | UU Serve Notice to Landowner                                          | 7d                 | 21-Jan-2026  | 29-Jan-2026 | 82d         |
| AMP8-DD&B-ROS-ECI-2530                                                                            | Land OwnerAgrees Early Entry                                          | 0d                 | 21-Jan-2026  |             | 4d          |
| Section 61                                                                                        |                                                                       | 5d                 | 19-Jan-2026  | 24-Jan-2026 | 109d        |
| Shaft 1                                                                                           |                                                                       | 5d                 | 19-Jan-2026  | 24-Jan-2026 | 82d         |
| AMP8-DD&B-ROS-ECI-2590                                                                            | UU Prepare and Issue Section 61                                       | 5d                 | 19-Jan-2026  | 23-Jan-2026 | 22d         |
| AMP8-DD&B-ROS-ECI-2620                                                                            | Section 61-Approval - Shaft 1                                         | 0d                 | 24-Jan-2026  |             | 119d        |
| Shaft 2                                                                                           |                                                                       | 5d                 | 19-Jan-2026  | 24-Jan-2026 | 80d         |
| AMP8-DD&B-ROS-ECI-2630                                                                            | UU Prepare and Issue Section 61                                       | 5d                 | 19-Jan-2026  | 23-Jan-2026 | 22d         |
| AMP8-DD&B-ROS-ECI-2650                                                                            | Section 61-Approval - Shaft2                                          | 0d                 | 24-Jan-2026  |             | 117d        |
| Shaft 3                                                                                           |                                                                       | 5d                 | 19-Jan-2026  | 24-Jan-2026 | 109d        |
| AMP8-DD&B-ROS-ECI-2660                                                                            | UU Prepare and Issue Section 61                                       | 5d                 | 19-Jan-2026  | 23-Jan-2026 | 22d         |
| AMP8-DD&B-ROS-ECI-2680                                                                            | Section 61-Approval - Shaft3                                          | 0d                 | 24-Jan-2026  |             | 159d        |
| Shaft 4                                                                                           |                                                                       | 5d                 | 19-Jan-2026  | 24-Jan-2026 | 49d         |
| AMP8-DD&B-ROS-ECI-2690                                                                            | UU Prepare and Issue Section 61                                       | 5d                 | 19-Jan-2026  | 23-Jan-2026 | 22d         |
| AMP8-DD&B-ROS-ECI-2710                                                                            | Section 61-Approval - Shaft4                                          | 0d                 | 24-Jan-2026  |             | 73d         |
| Shaft 5                                                                                           |                                                                       | 5d                 | 19-Jan-2026  | 24-Jan-2026 | 24d         |
| AMP8-DD&B-ROS-ECI-2720                                                                            | UU Prepare and Issue Section 61                                       | 5d                 | 19-Jan-2026  | 23-Jan-2026 | 22d         |
| AMP8-DD&B-ROS-ECI-2740                                                                            | Section 61-Approval - Shaft5                                          | 0d                 | 24-Jan-2026  |             | 34d         |
| Shaft 7                                                                                           |                                                                       | 5d                 | 19-Jan-2026  | 24-Jan-2026 | 22d         |
| AMP8-DD&B-ROS-ECI-2750                                                                            | UU Prepare and Issue Section 61                                       | 5d                 | 19-Jan-2026  | 23-Jan-2026 | 22d         |
| AMP8-DD&B-ROS-ECI-2770                                                                            | Section 61-Approval - Shaft7                                          | 0d                 | 24-Jan-2026  |             | 32d         |
| Ground Investigation Shaft Boreholes                                                              |                                                                       | 40d                | 26-Jan-2026  | 20-Mar-2026 | 24d         |
| Shaft 7 West Way                                                                                  |                                                                       | 19d                | 26-Jan-2026  | 19-Feb-2026 | 6d          |
| AMP8-DD&B-ROS-ECI-1390                                                                            | Ground Investigation - Shaft7 WestWay - 2 Boreholes 5 Feb             | 19d                | 26-Jan-2026  | 19-Feb-2026 | 6d          |
| Shaft 5 West Way                                                                                  |                                                                       | 18d                | 28-Jan-2026  | 20-Feb-2026 | 6d          |
| AMP8-DD&B-ROS-ECI-1370                                                                            | Ground Investigation Shaft5 - WestWay - 2 Boreholes 5 Feb             | 18d                | 28-Jan-2026  | 20-Feb-2026 | 6d          |
| Shaft 3 Cardinal Allen High School                                                                |                                                                       | 33d                | 04-Feb-2026  | 20-Mar-2026 | 24d         |
| AMP8-DD&B-ROS-ECI-1470                                                                            | Delay - Landfill site issue - EWN 18                                  | 18d                | 04-Feb-2026  | 27-Feb-2026 | 24d         |
| AMP8-DD&B-ROS-ECI-1350                                                                            | Ground Investigation Shaft3 - CardinalAllen High School - 2 Boreholes | 5d                 | 02-Mar-2026  | 06-Mar-2026 | 24d         |
| AMP8-DD&B-ROS-ECI-1410                                                                            | Ground Investigation Report                                           | 10d                | 09-Mar-2026  | 20-Mar-2026 | 24d         |
| Shaft 2 BroadWater Wood                                                                           |                                                                       | 25d                | 16-Feb-2026  | 20-Mar-2026 | 24d         |
| AMP8-DD&B-ROS-ECI-1440                                                                            | Delay - Landfill site Issue - EWN18                                   | 10d                | 16-Feb-2026* | 27-Feb-2026 | 24d         |
| AMP8-DD&B-ROS-ECI-1340                                                                            | Ground Investigation Shaft2 - Broadwater Woods - 2 Boreholes          | 5d                 | 02-Mar-2026  | 06-Mar-2026 | 24d         |
| AMP8-DD&B-ROS-ECI-1400                                                                            | Ground Investigation Report                                           | 10d                | 09-Mar-2026  | 20-Mar-2026 | 24d         |
| Shaft 1 Fleetwood Works                                                                           |                                                                       | 25d                | 16-Feb-2026  | 20-Mar-2026 | 24d         |

Remaining Level of Effort Construction summary, Team #1 Construction summary, Team #2 Construction summary, Team #3 Actual Level of Effort

Actual ... Remai... Critical... Milesto...

Programme ref: Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31  
Project ID: UU-AMP8-ROSS-DEL-1002-001978-1

Data Date: 24-Nov-2025  
Page 4 of 11

| Date        | Revision     | Checked | Approved |
|-------------|--------------|---------|----------|
| 23-Feb-2026 | Rossall CL31 | SI      |          |






| <div> <div> <div>Remaining Level of Effort</div> <div>Construction summary, Team #1</div> <div>Construction summary, Team #2</div> <div>Construction summary, Team #3</div> <div>Actual Level of Effort</div> </div> <div> <div>Actual ...</div> <div>Remai...</div> <div>Critical...</div> <div>Milesto...</div> </div> </div> | <div> <div>Programme ref: Rossall Outfall Pipe Installation &amp; Relining- 24th Nov 25 - CL 31</div> <div>Project ID: UU-AMP8-ROSS-DEL-1002-001978-1</div> </div> | <div> <div>Data Date: 24-Nov-2025</div> <div>Page 5 of 11</div> </div> | <table border="1"> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> <tr> <td>23-Feb-2026</td> <td>Rossall CL31</td> <td>SI</td> <td></td> </tr> <tr> <td colspan="4"></td> </tr> </table> | Date | Revision | Checked | Approved | 23-Feb-2026 | Rossall CL31 | SI |  |  |  |  |  |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------|----------|---------|----------|-------------|--------------|----|--|--|--|--|--|
| Date                                                                                                                                                                                                                                                                                                                            | Revision                                                                                                                                                           | Checked                                                                | Approved                                                                                                                                                                                                               |      |          |         |          |             |              |    |  |  |  |  |  |
| 23-Feb-2026                                                                                                                                                                                                                                                                                                                     | Rossall CL31                                                                                                                                                       | SI                                                                     |                                                                                                                                                                                                                        |      |          |         |          |             |              |    |  |  |  |  |  |
|                                                                                                                                                                                                                                                                                                                                 |                                                                                                                                                                    |                                                                        |                                                                                                                                                                                                                        |      |          |         |          |             |              |    |  |  |  |  |  |



UU-AMP8-ROSS-DEL-1002-001978-1


Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

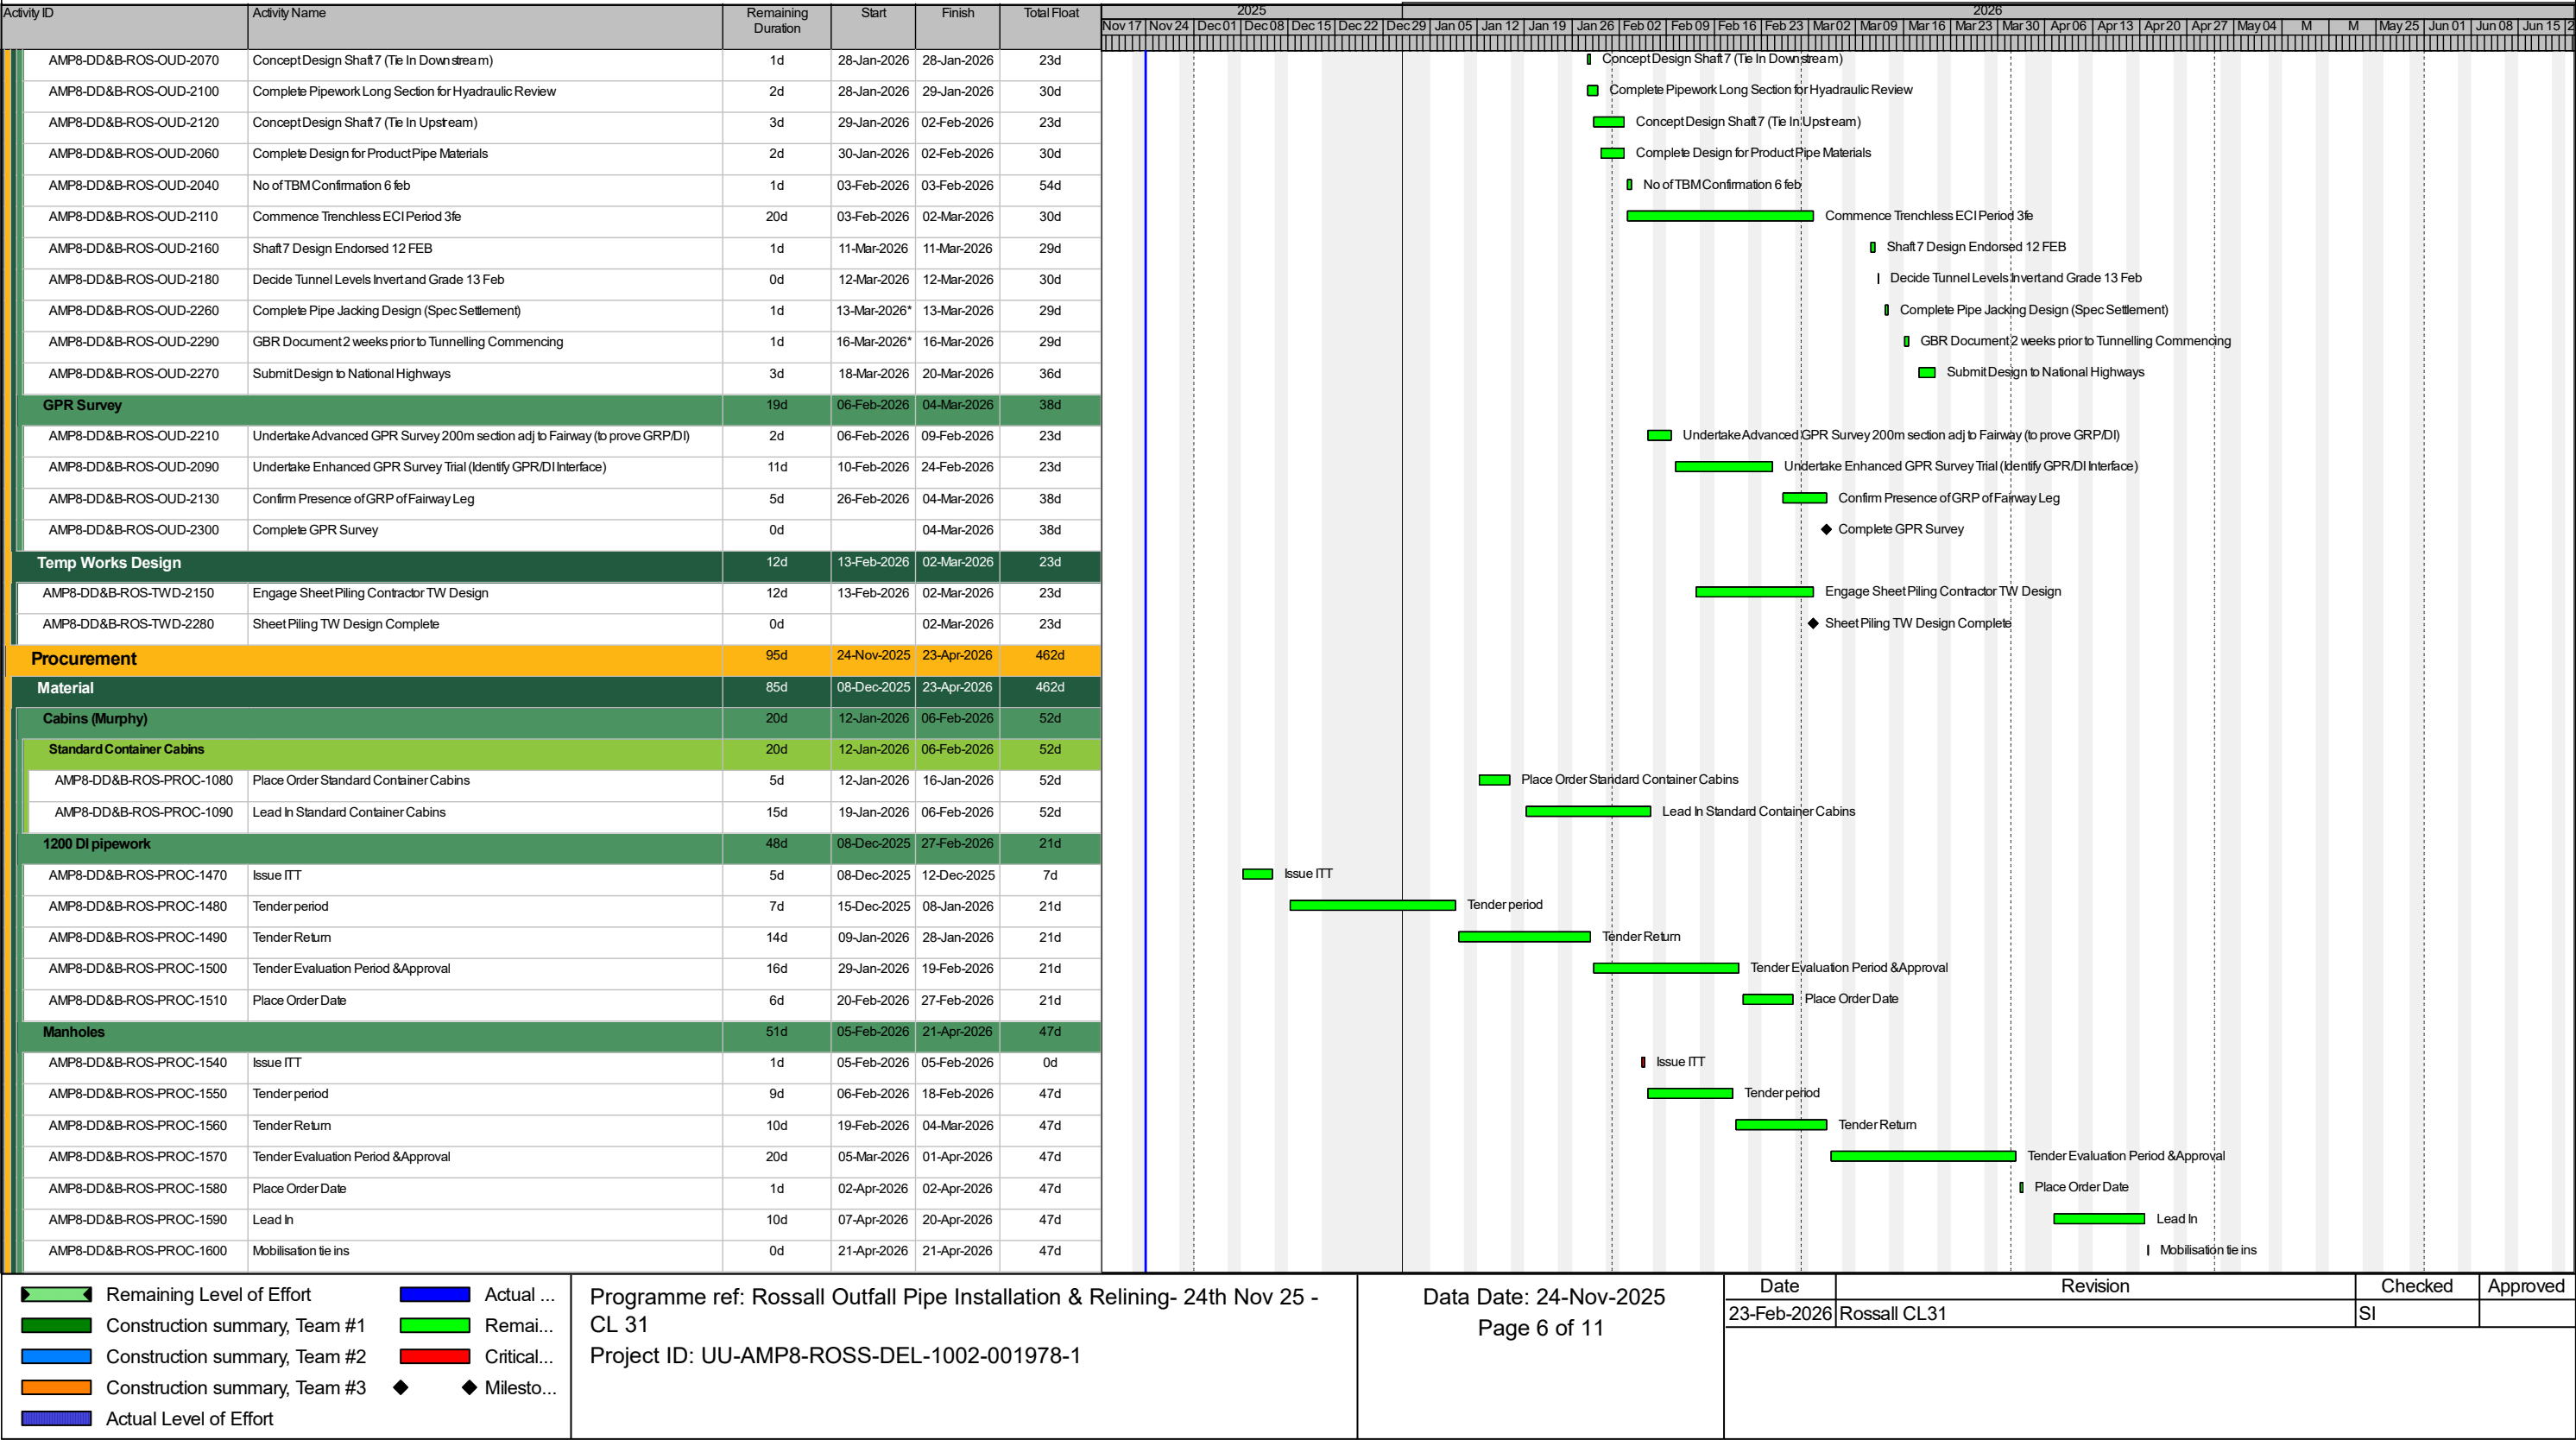



UU-AMP8-ROSS-DEL-1002-001978-1


Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

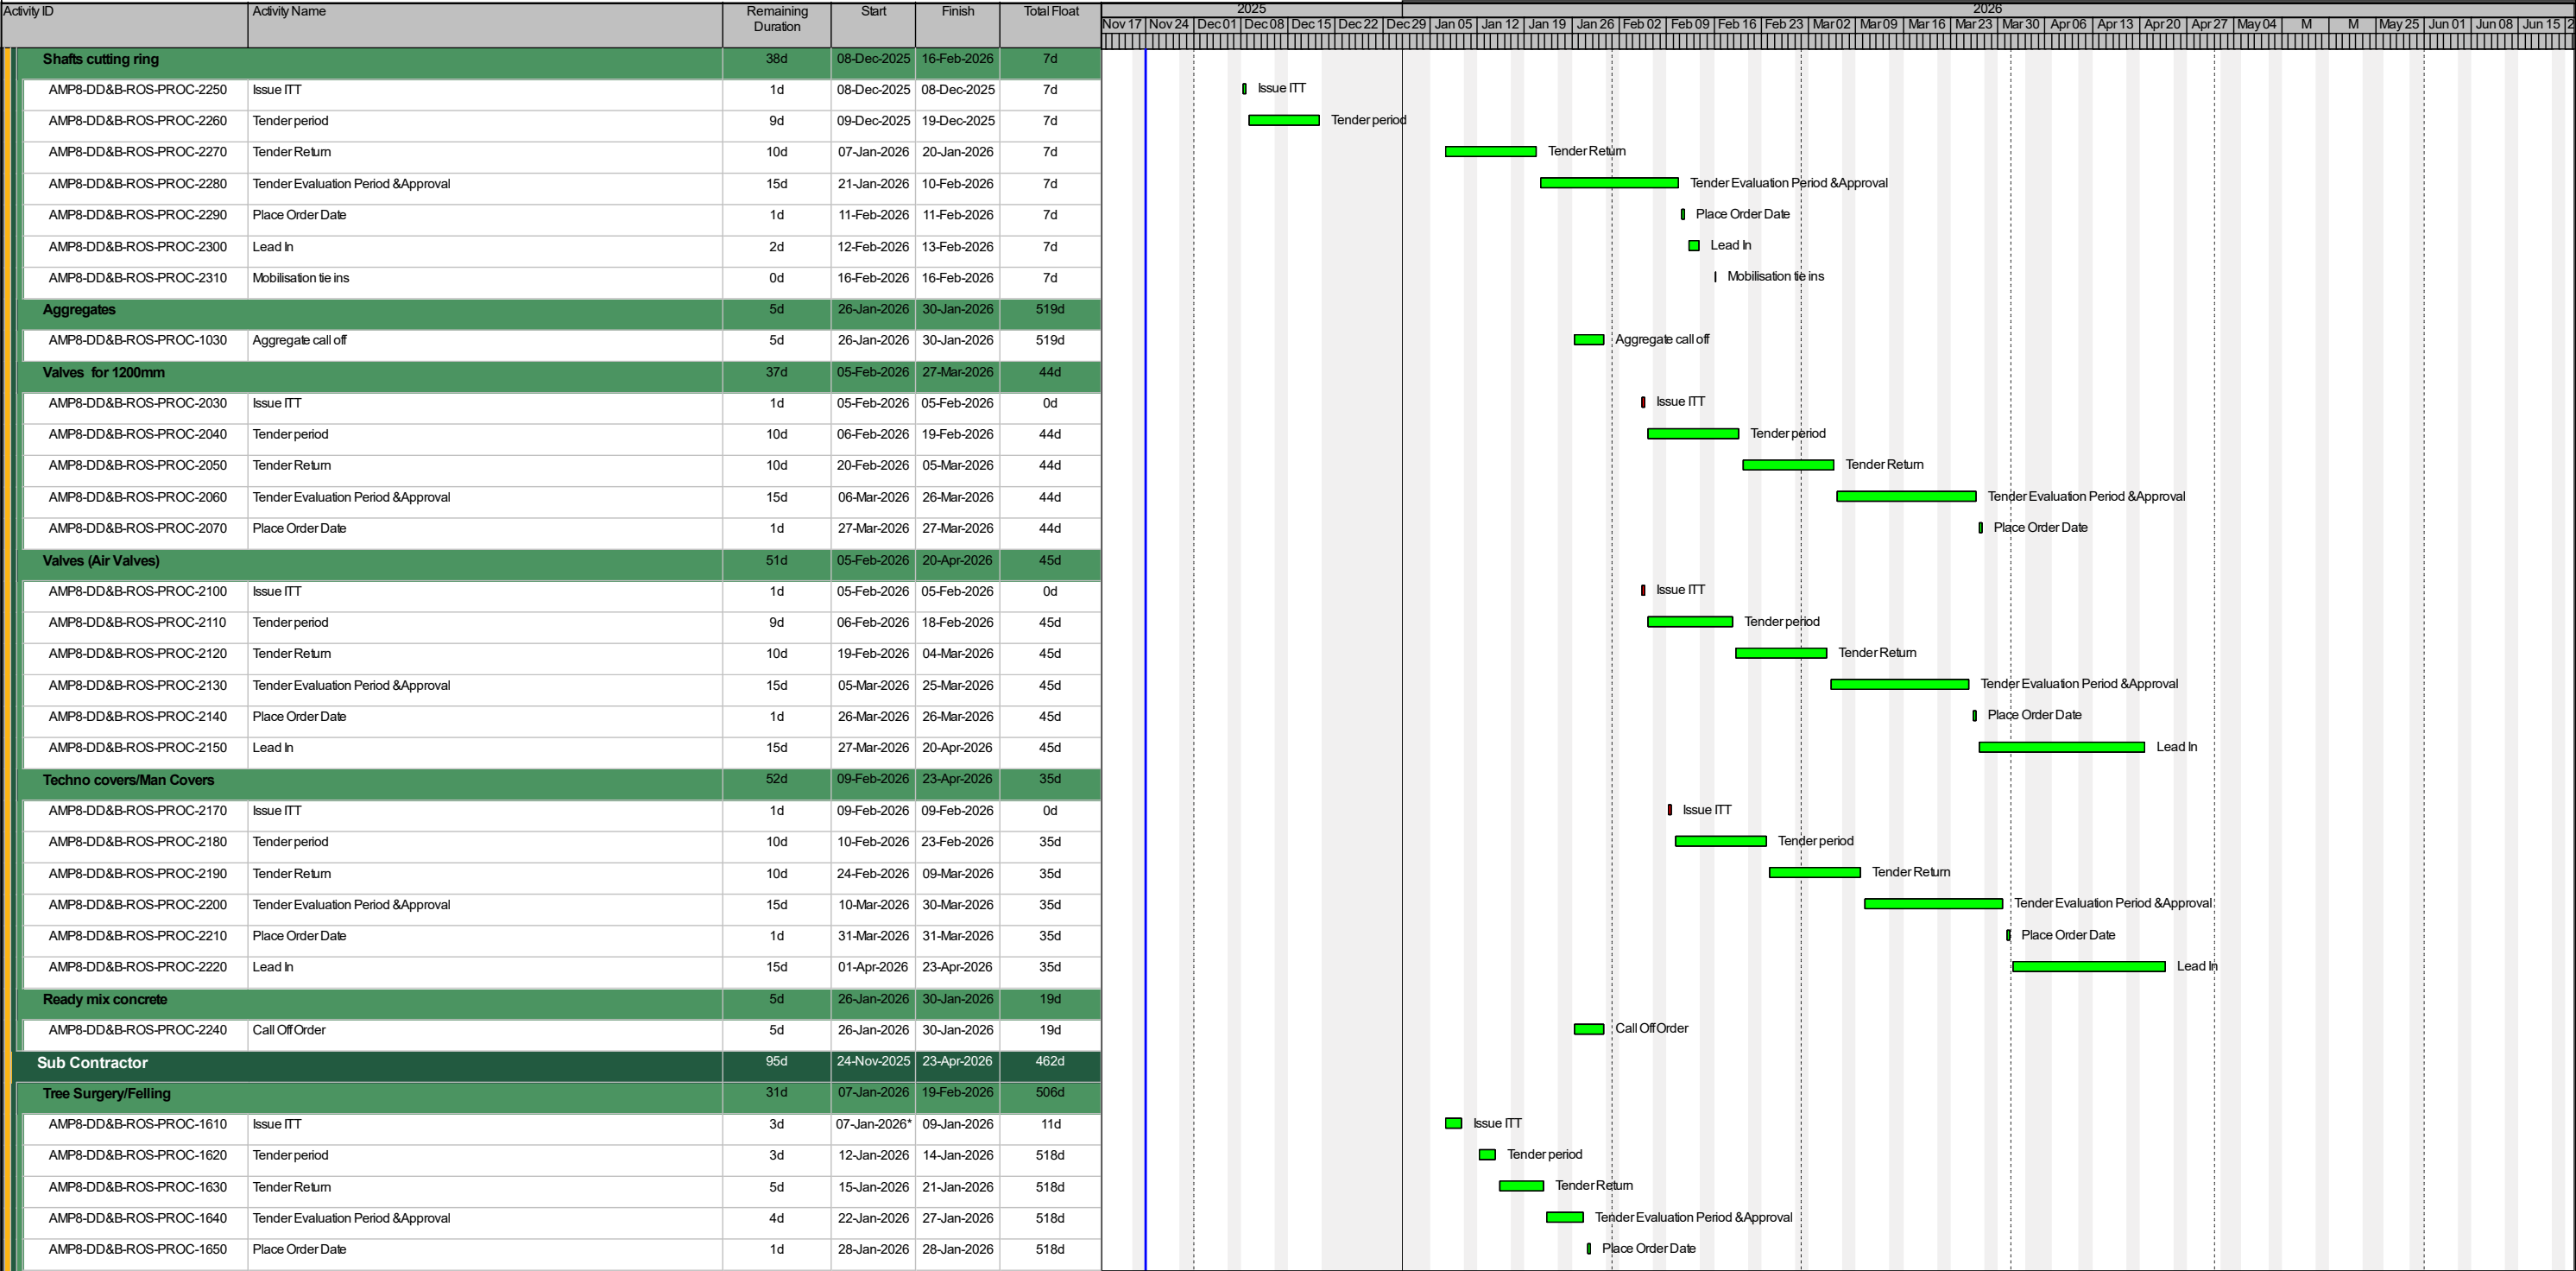



UU-AMP8-ROSS-DEL-1002-001978-1

Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

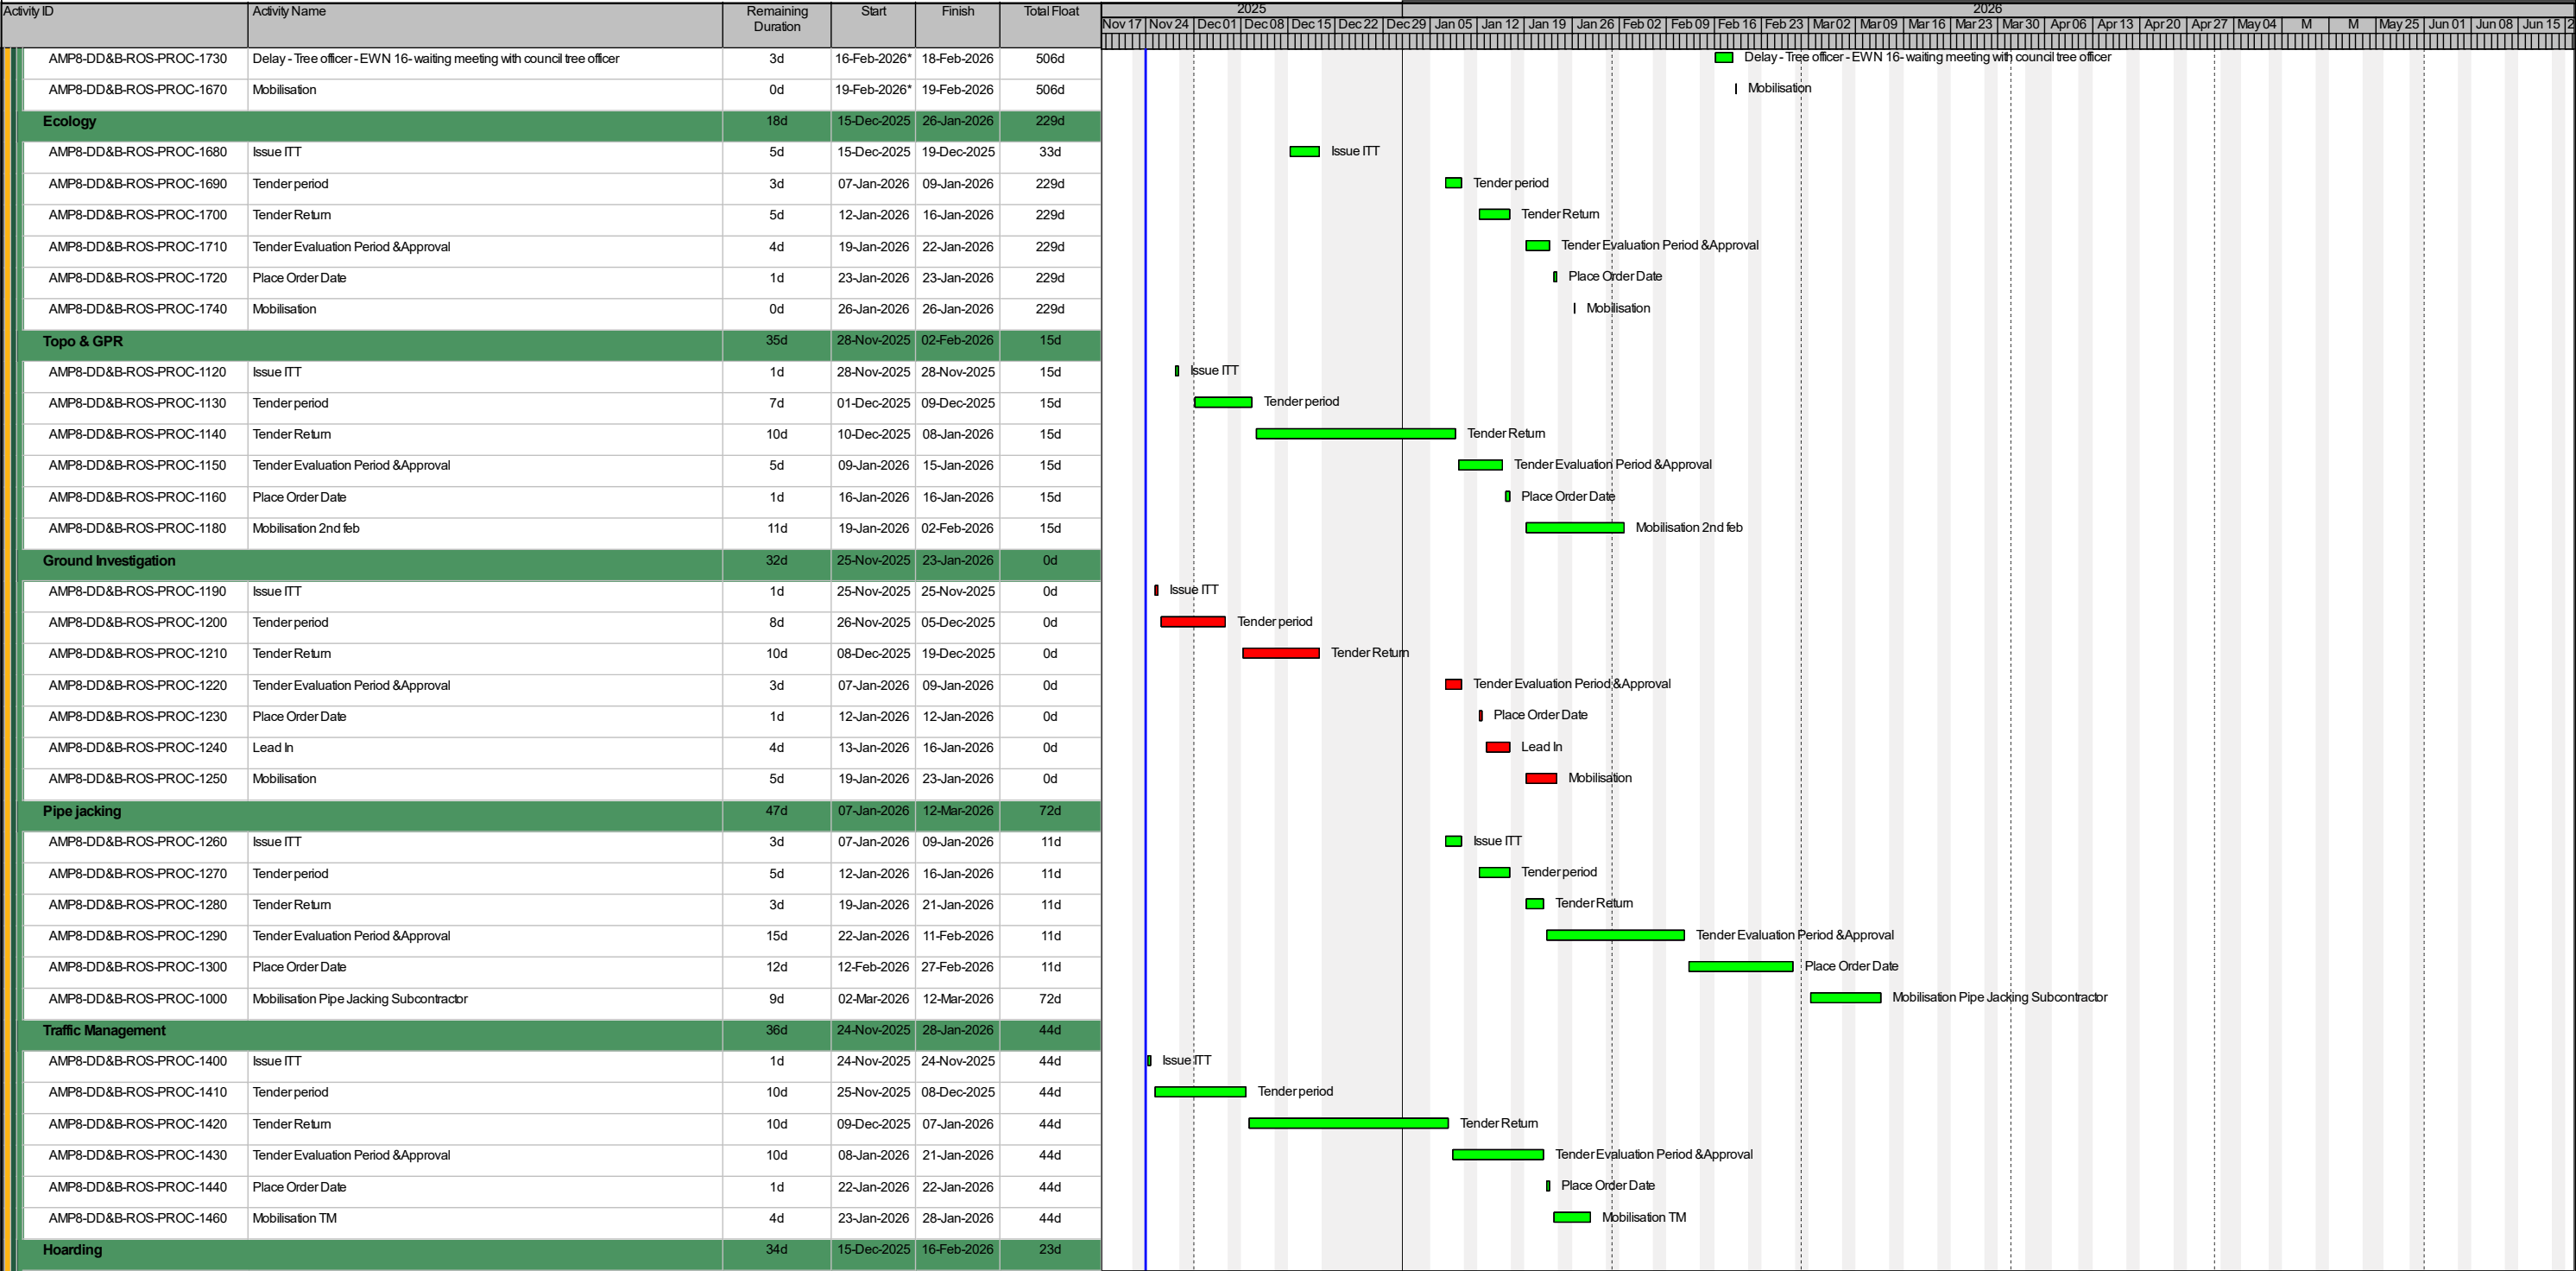






UU-AMP8-ROSS-DEL-1002-001978-1


Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

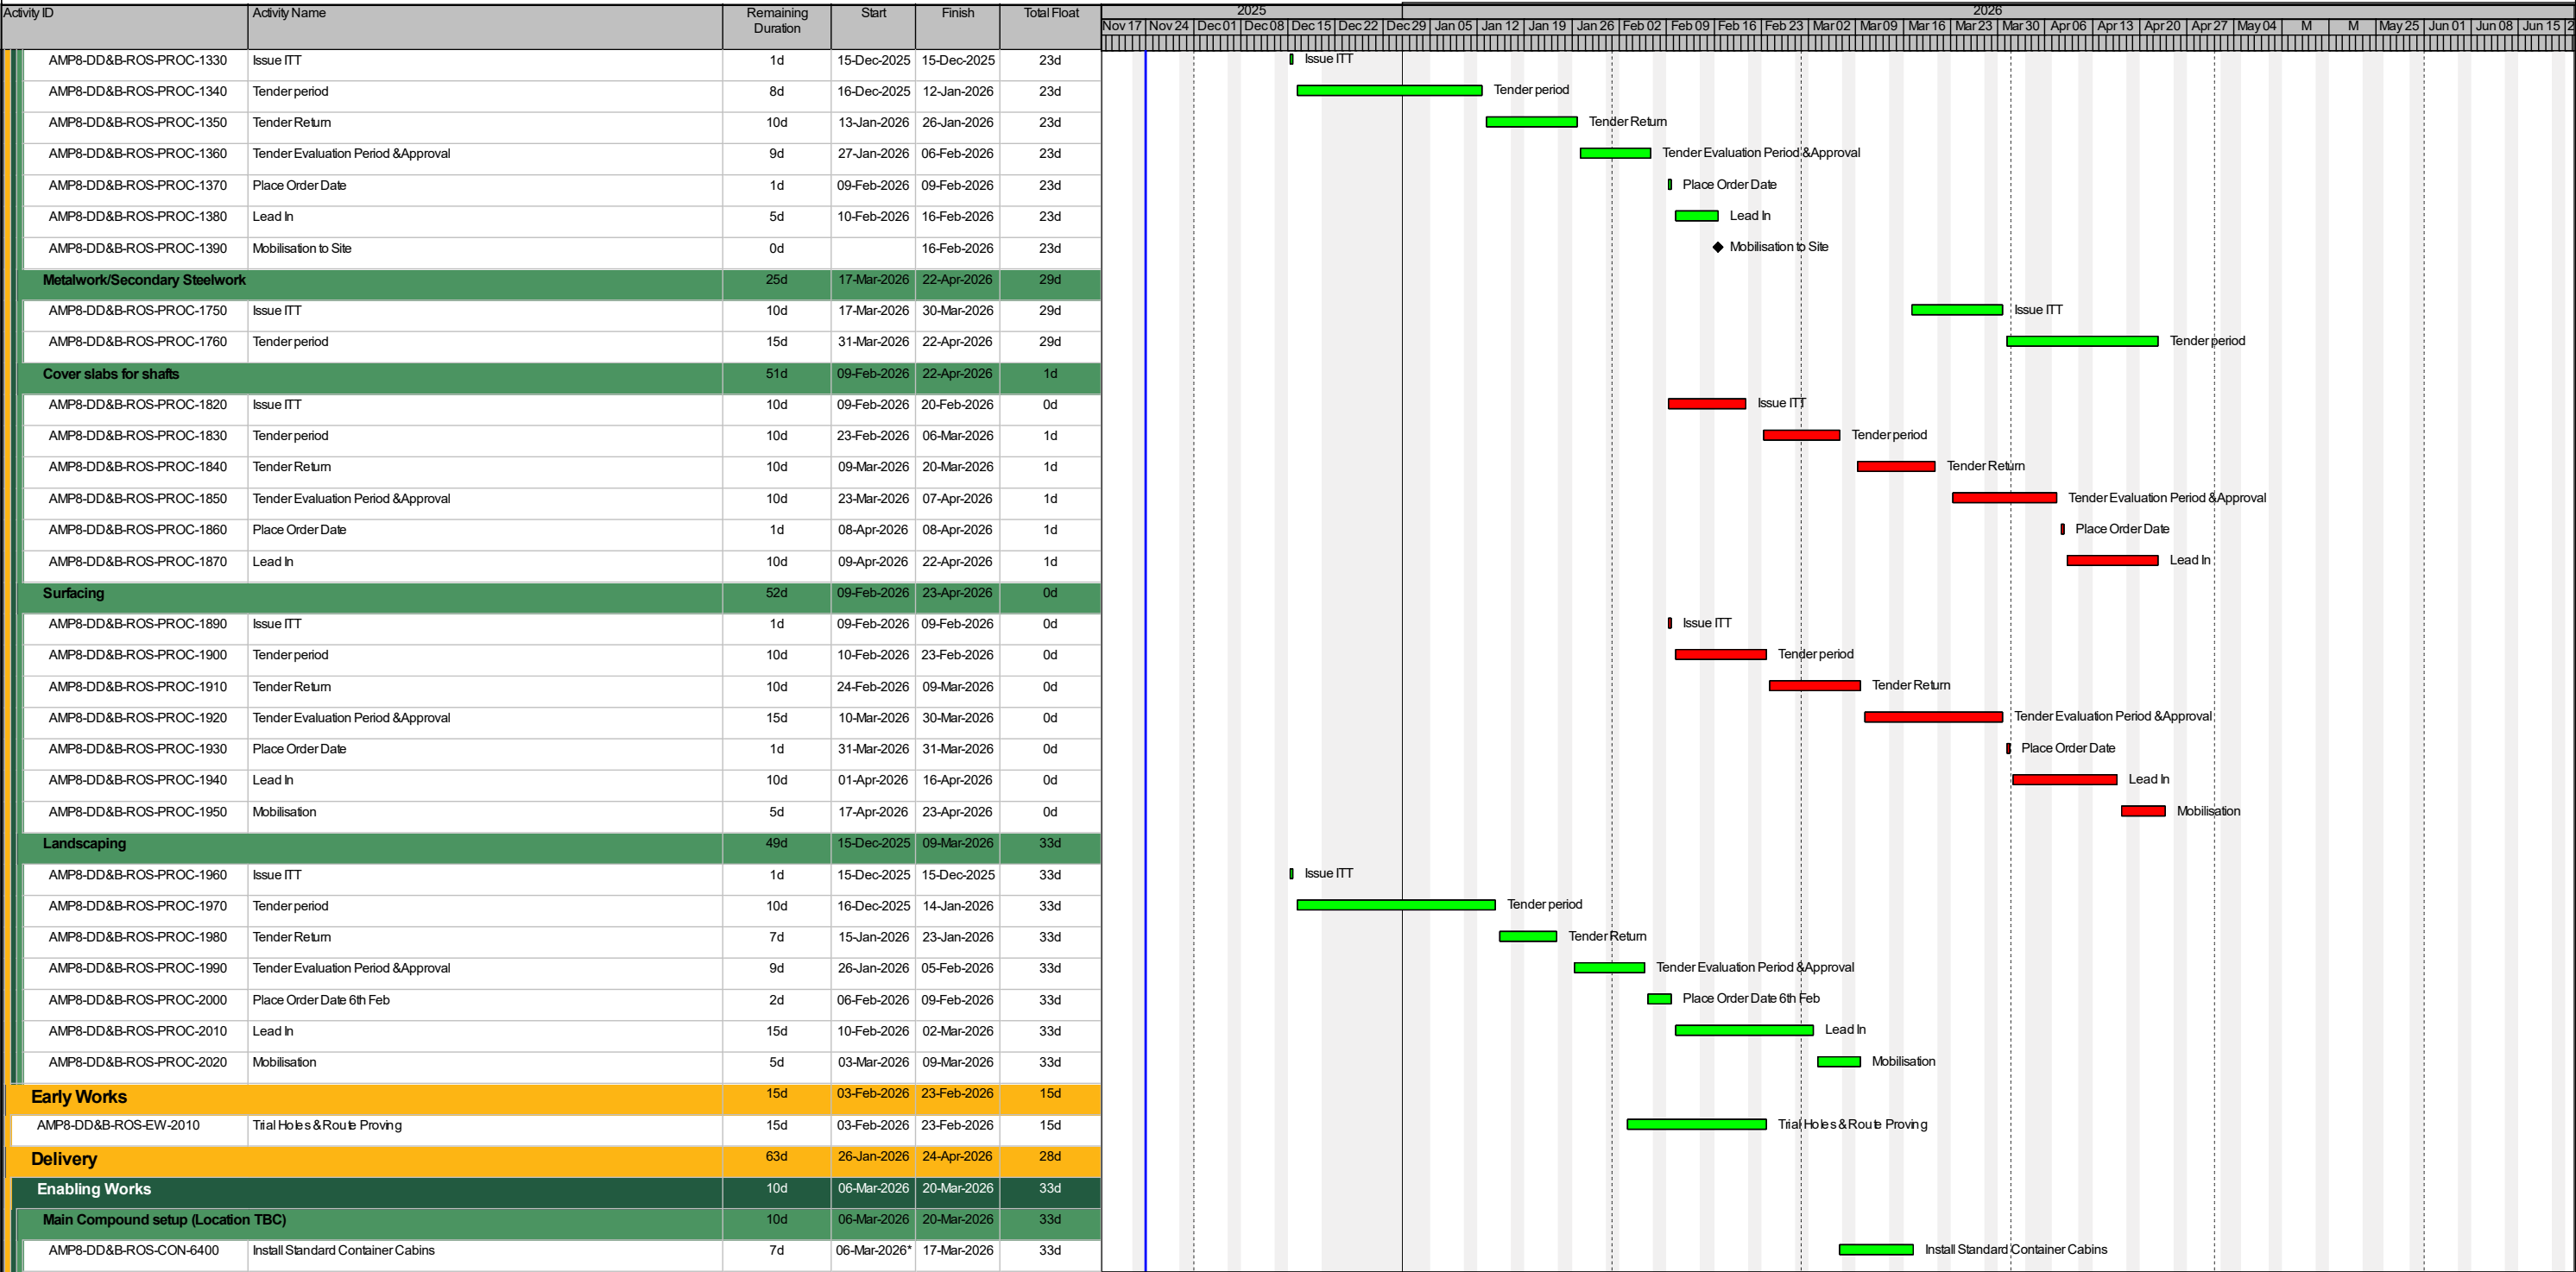



UU-AMP8-ROSS-DEL-1002-001978-1

Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

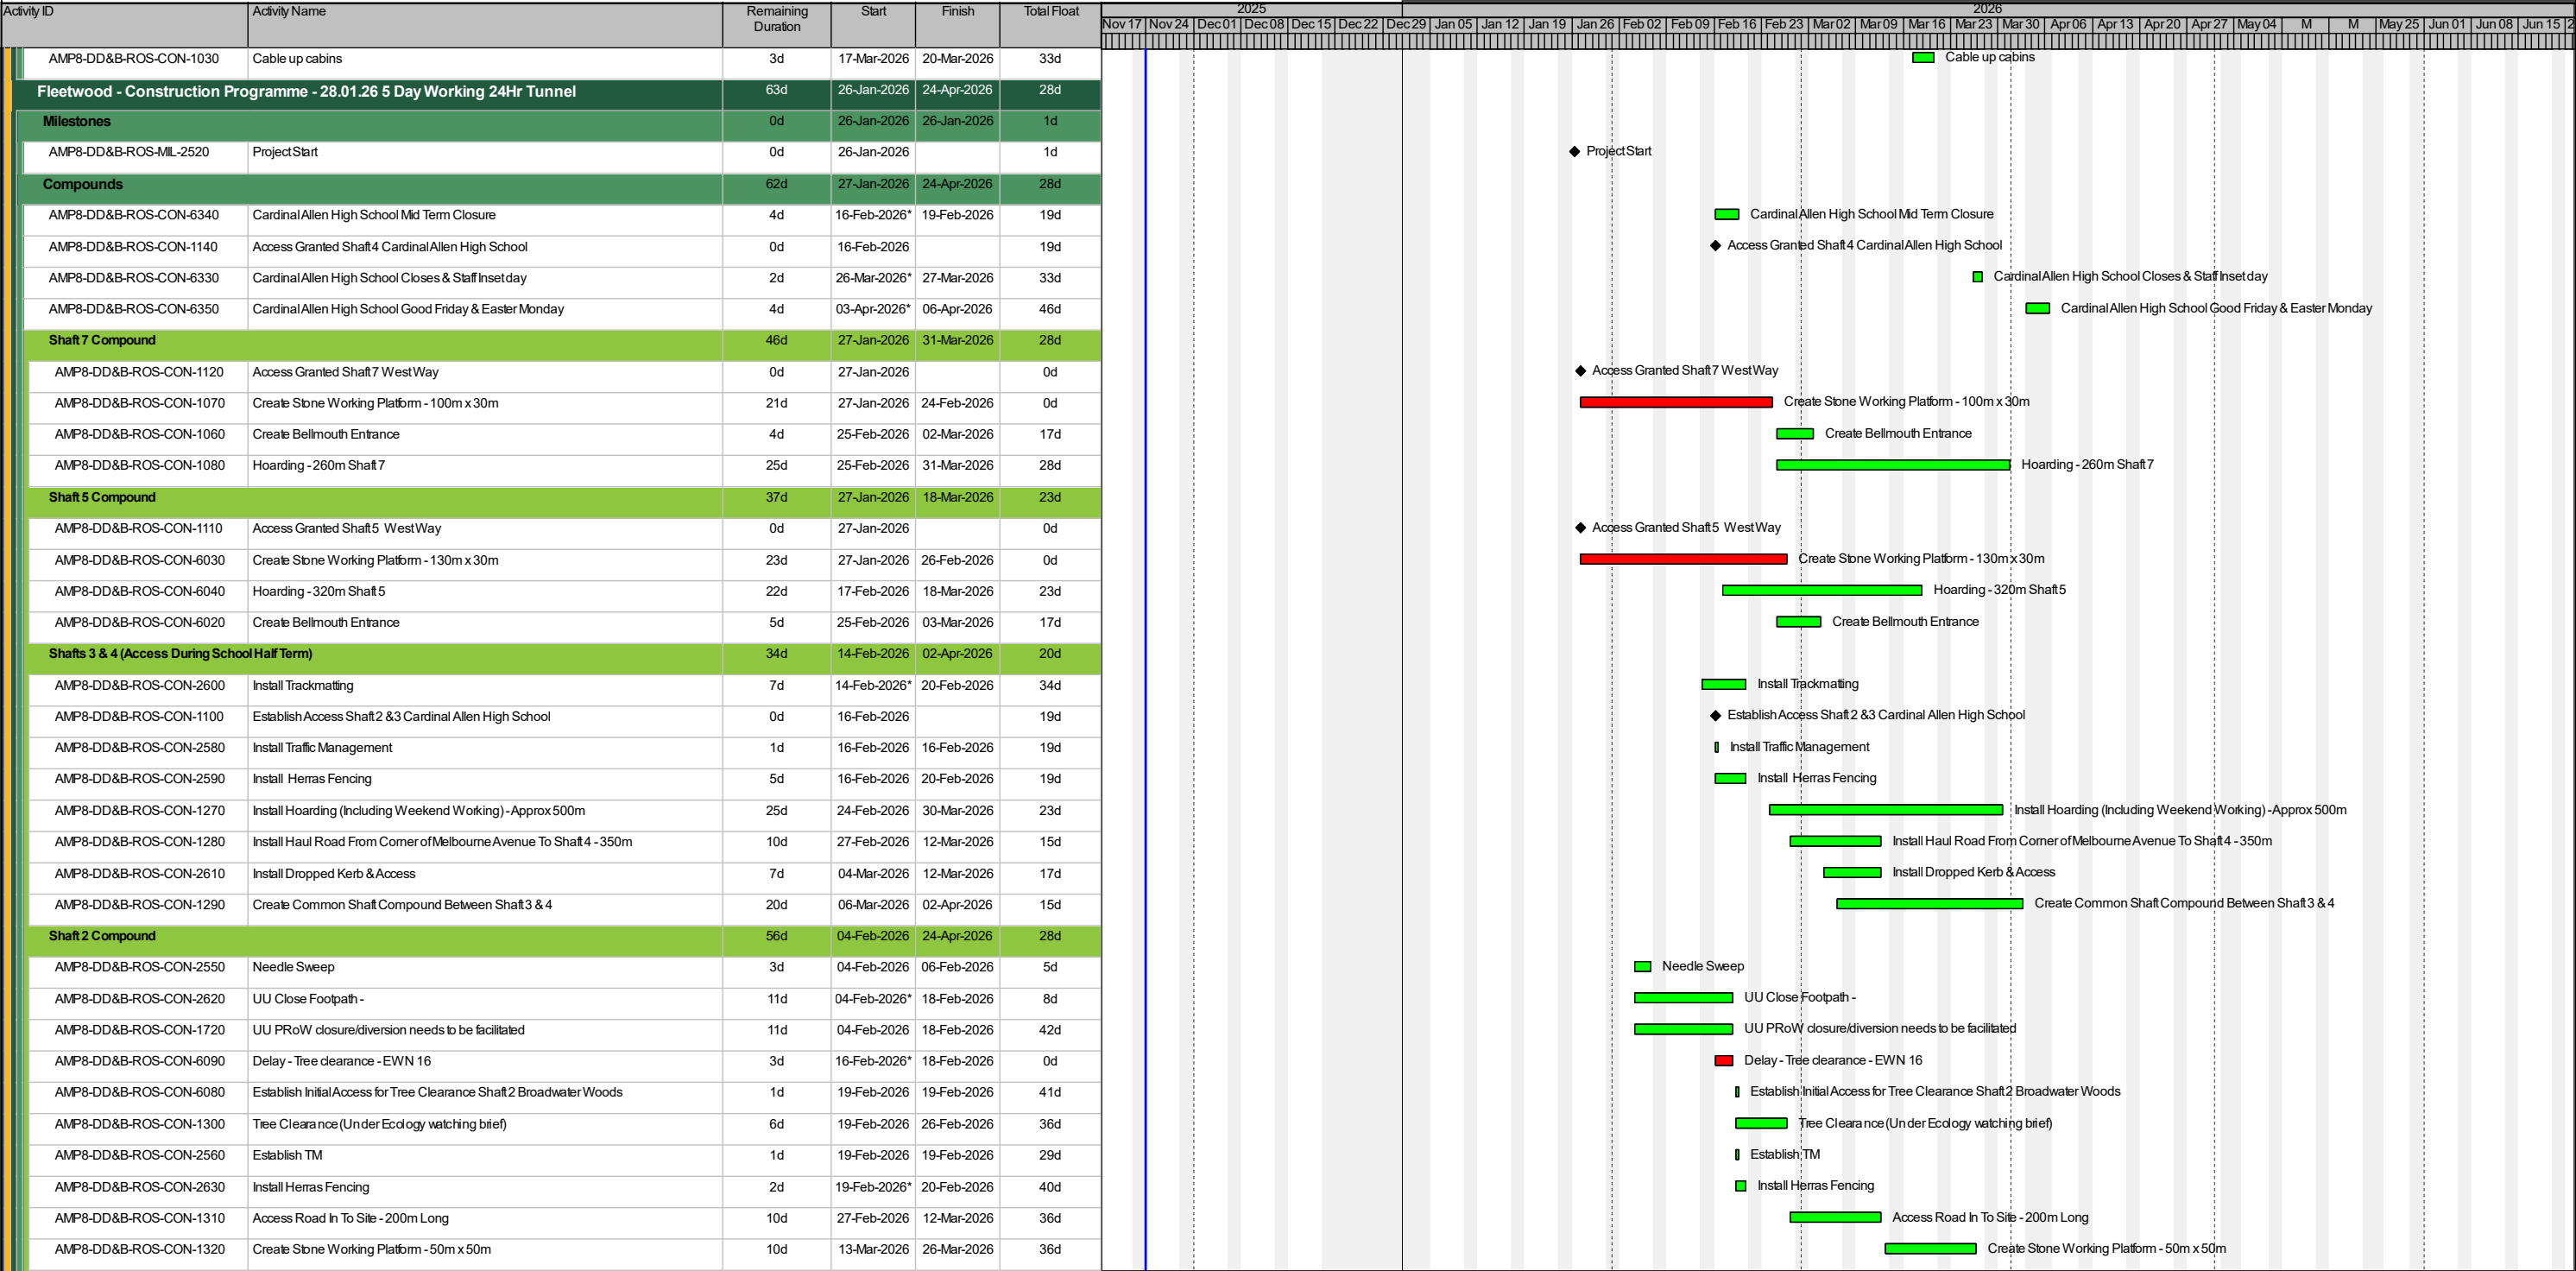

|                                                                                                                                                                                                                                                               |                                                                                                                                        |                                                                                                                                |                                         |      |          |         |          |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------|------|----------|---------|----------|
| <div><div></div> Remaining Level of Effort</div> <div><div></div> Construction summary, Team #1</div> <div><div></div> Construction summary, Team #2</div> <div><div></div> Construction summary, Team #3</div> <div><div></div> Actual Level of Effort</div> | <div><div></div> Actual ...</div> <div><div></div> Remai...</div> <div><div></div> Critical...</div> <div><div></div> Milesto...</div> | Programme ref: Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31<br>Project ID: UU-AMP8-ROSS-DEL-1002-001978-1 | Data Date: 24-Nov-2025<br>Page 10 of 11 | Date | Revision | Checked | Approved |
| 23-Feb-2026                                                                                                                                                                                                                                                   | Rossall CL31                                                                                                                           |                                                                                                                                |                                         | SI   |          |         |          |
|                                                                                                                                                                                                                                                               |                                                                                                                                        |                                                                                                                                |                                         |      |          |         |          |



Rossall Outfall Pipe Installation & Relining- 24th Nov 25 - CL 31

